

Measure L

City Name: Ceres

Project Name: Richland Sidewalk and Roadway Improvement

Date: Q2 : 10/1/25 to 12/31/25

Project Revenue		Q2 Measure L (ML) Expenses (EXP)	
City Funds	\$0.00	Budgeted ML Funds	\$150,000.00
Federal Funds	\$0.00	Encumbered/Prior EXP	\$17,500.00
State Funds	\$0.00	ML Funds Expended	\$2,998.72
Measure L Funds	\$150,000.00	ML Funds Available	\$129,501.28
Other Funds	\$0.00		
Total	\$150,000.00	Total	\$20,498.72

Phase:

Design


Overall Project Details:

The project proposes to perform pavement rehabilitation on Richland Avenue, from Hatch Road to Herndon Avenue, approximately 0.6 mile. The project includes areas of fatigue of the existing pavement, reconstruction of curb ramps to meet ADA compliance, removal and replacement of damaged curb & gutter, pavement marking & striping, and other associated improvements necessary to improve the roadway condition.

Project Status:

In Design

Add photos/renderings:

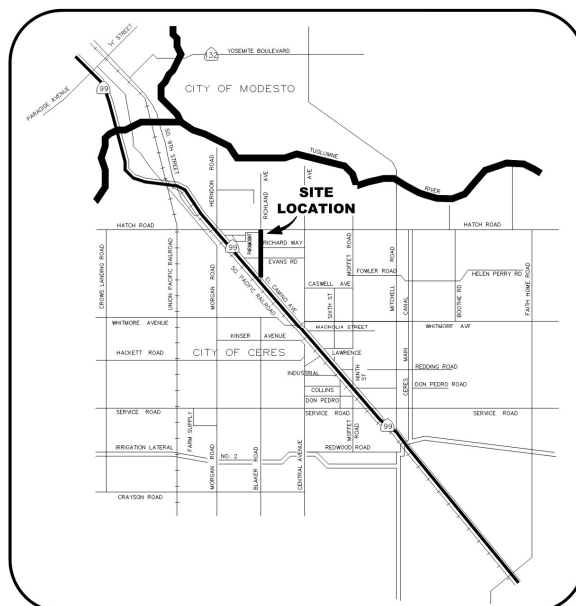

LOCATION MAP
